



AGENDA ITEM EXECUTIVE SUMMARY

Title: Presentation to Provide Update on Proposed IL Route 64 Projects

Presenter: James Bernahl

Please check appropriate box:

<input type="checkbox"/>	Government Operations	<input checked="" type="checkbox"/>	Government Services 04.23.12
<input type="checkbox"/>	Planning & Development	<input type="checkbox"/>	City Council

Estimated Cost: _____ Budgeted: YES NO

If NO, please explain how item will be funded:

Executive Summary:

The following presentation will provide the most up to date information to the City Council relative to the following IL Route 64 Projects:

(See Attached Memo)

Attachments: *(please list)*

IL Route 64 Project Update Memo
IDOT Website Page

Recommendation / Suggested Action *(briefly explain):*

Presentation is for informational purposes only.

For office use only: Agenda Item Number: 5.a

IL Route 64 Project Update Memo

1. IL Route 64 and Oak Street Intersection Improvements

Staff is currently coordinating with the contractor (Curran Paving) on the relocation of existing City electrical appurtenances, as well as AT&T utility items. Construction work is expected to begin towards the end of this month beginning with the installation of new storm and sanitary sewers, and roadway removal. Construction notification letters and roadway notification signs will be in place shortly.

2. IL Route 64 - (7th to Kirk Road) Project and IL Route 64 – (Kautz Road to Route 59) Project

On March 2, 2012 staff participated in the IDOT Preconstruction meeting for both of the IL 64 Projects (7th Ave. to Dunham Rd.) and (Dunham Rd. to IL 59). The following items were highlights taken from that meeting.

Meeting Highlights:

- Gabriel Couris, Community Relations Manager from IDOT, is delivering flyers to the local businesses along the IL 64 corridor which will be affected by the construction within the next few weeks.
- IDOT in collaboration with the City will be hosting an open house meeting, on April 24, 2012 at the City Hall, for the local businesses along the IL 64 corridor only. IDOT has specified that they only want to focus on meeting with the businesses and Chambers of Commerce so as to focus on their specific needs. General resident questions and concerns can be directed to James Bernahl.
- Benesch will be the IDOT Resident Engineering consultant for both of these projects which should help to control overall construction activities.
- The General Contractor for these two projects is Martam Construction from Elgin. The Contractor is working on preparing the emergency contact list for IDOT.
- The City will be participating in weekly progress meetings with the Contractor and IDOT personnel.

Start Dates:

- IL 64 (7th Avenue to Dunham) - Scheduled to begin April 16, 2012 with message boards being placed one week prior. During the first two weeks most activity will involve material and equipment deliveries and surveying activities. A comment was made that it is "estimated" that actual roadway closures and roadway removal activities will most likely begin May 1.
- IL 64 (Dunham to IL 59) - Scheduled to begin April 23, 2012. Similar to notes mentioned previously with message boards going up one week prior to that date.

Completion Dates:

- IL 64 (7th Avenue to Dunham) - July 26, 2013
- IL 64 (Dunham to IL 59) - August 31, 2013

Note: All remaining off-site water main work is being coordinated with the IDOT Contractor and is scheduled to begin in May 2012.



Illinois Route 64 Improvement Project



7th Avenue to Illinois 59

PROJECT OVERVIEW

The Illinois Department of Transportation (IDOT) plans to reconstruct, widen, and resurface Illinois Route 64 from 7th Avenue on the western limits to Illinois 59 on the eastern limits. Illinois Route 64 improvements will include a bridge reconstruction, lighting, addition of retaining walls, and sidewalk additions. Illinois Route 64 construction will alleviate congestion and improve driver safety throughout the project limits.

The purpose of the \$49.1 million dollar project is to enhance the flow of traffic and reduce the potential for accidents. The goal of Illinois Route 64 reconstruction is to provide a safer ride for the motoring public. Motorists should expect delays and use caution when workers are present. IDOT suggests using alternate routes and public transportation.



Project Start Date: **Late April 2012**
Project End Date: **Fall, 2013**
Project Cost: **\$49,186,022.81**
Project Length: **5.2 miles**
Project Municipality: **St. Charles, West Chicago**
Project County: **DuPage, Kane**

The link below has been created to provide one location where the public can get details about the Illinois Route 64 project scope and the construction staging and schedule. The information is intended to help you understand what we will be doing and when the work is anticipated to take place.

As the Department works to make this section of roadway safer for the future, we want to make sure users, residents and local business owners have up to date information on the progress of the project. If you have any questions about the project that have not been answered with the information on this site please use the "Contact Us" section and a response will be sent to you.



For any questions or concerns regarding the Illinois Route 64 (North Ave.) project, please visit our website

www.dot.state.il.us/IL64/index.html



Illinois Route 64 Improvement Project

Project Limits: 7th Avenue to Illinois 59
City of St. Charles and City of West Chicago

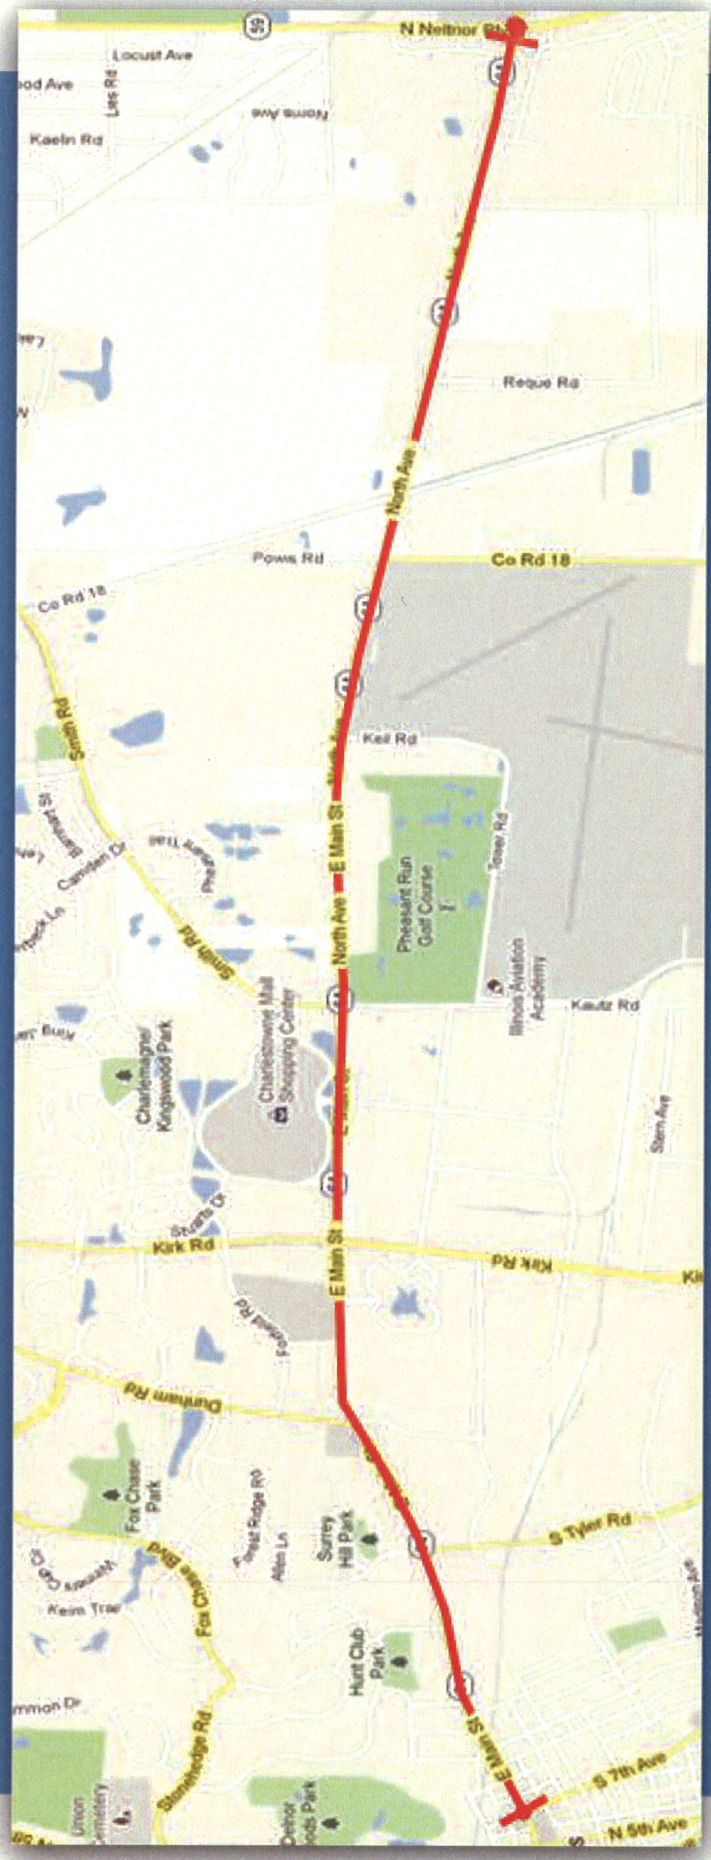

Project Limits
