
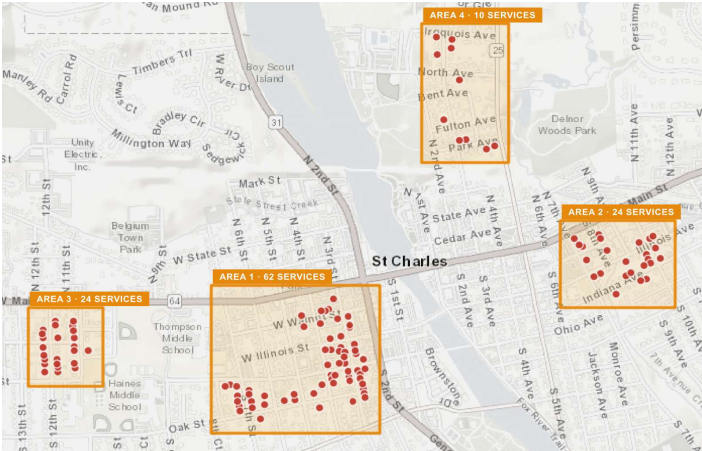
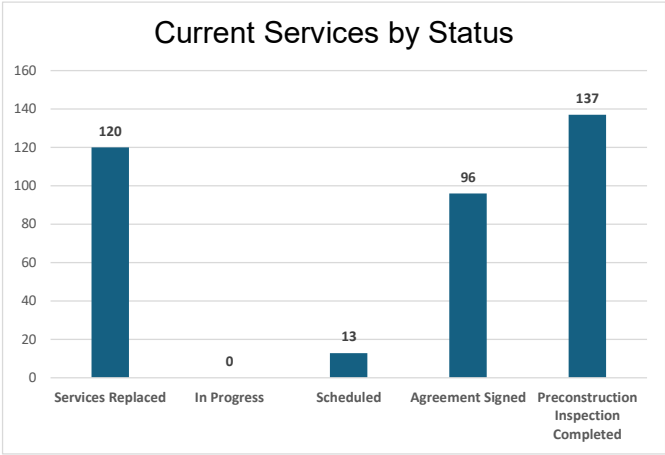
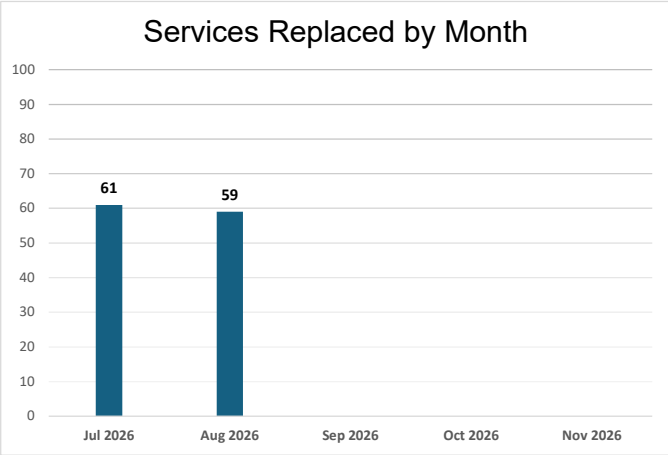
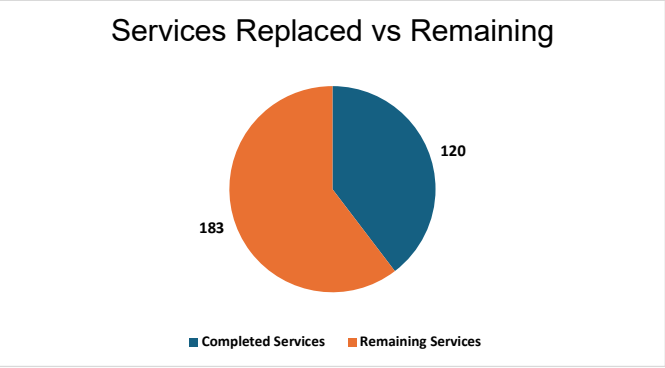


City of St. Charles 2026 Lead Service Line Replacement Program


AUGUST 2026 REPORT | July 28, 2026 - August 28, 2026

Approved Budget	Completed Cost To Date	Remaining Budget	Budget %	Services Completed	Services Remaining	Service Completion %
\$ 7,650,000.00	\$ 2,303,260.50	\$ 5,346,739.50	30.1%	120	183	39.6%

Service Current Status Summary						
Total Services	Services Replaced	In Progress	Scheduled	Agreements Signed	Preconstruction Inspections Completed	Door Hangers Distributed and Resident Contacts Made
303	120	0	13	96	137	146

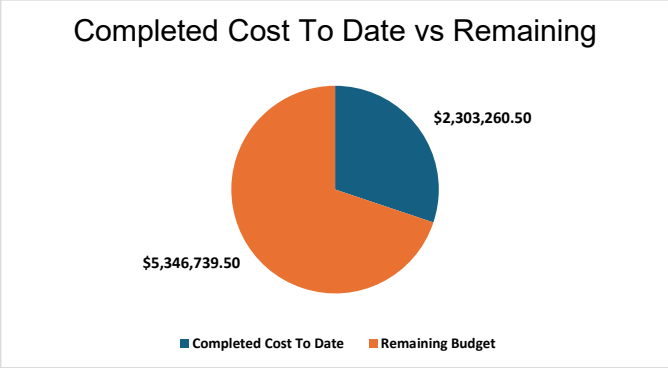

CURRENT WORK AREAS

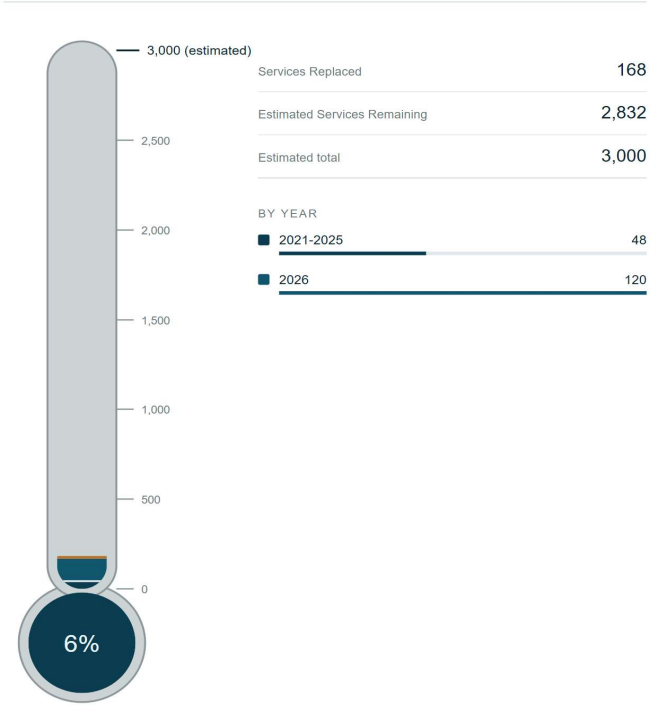

Data as of August 28, 2026
