
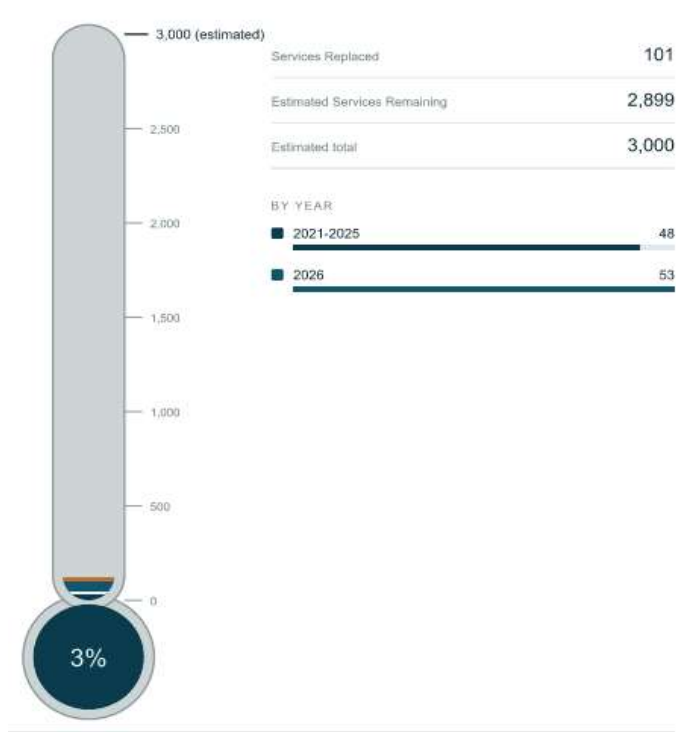
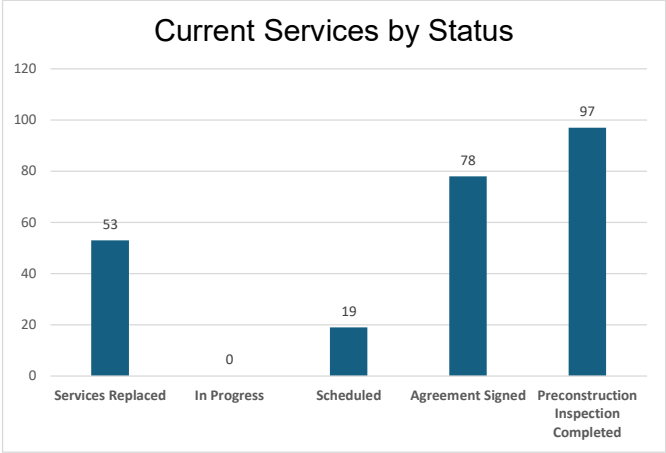
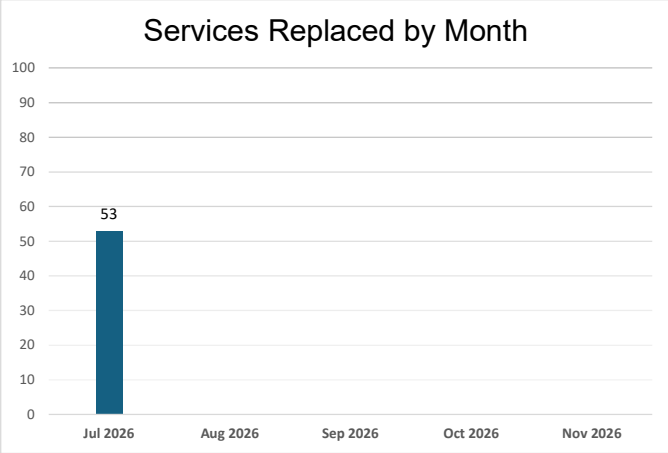
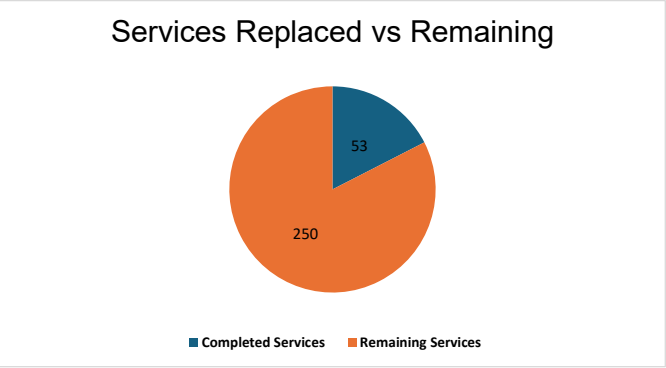


City of St. Charles 2026 Lead Service Line Replacement Program

JULY 2026 REPORT | July 8, 2026 - July 27, 2026

Approved Budget	Completed Cost To Date	Remaining Budget	Budget %	Services Completed	Services Remaining	Service Completion %
\$7,650,000	\$0	\$7,650,000	0.0%	53	250	17.5%

Service Current Status Summary						
Total Services	Services Replaced	In Progress	Scheduled	Agreements Signed	Preconstruction Inspection Completed	Door Hangers Distributed and Resident Contacts Made
303	53	0	19	78	97	146

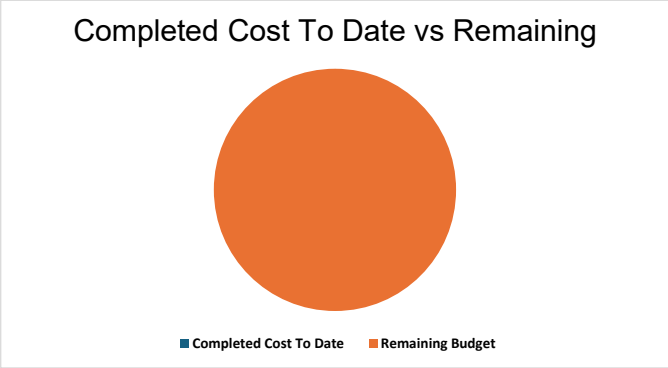

Data as of July 29, 2026

OVERALL SERVICE REPLACEMENT PROGRESS
